

Summer Capital Projects

July 20, 2022



High School

SSHS	Handicapped Access at Main Entrance- In progress
SSHS	Repaint and line track- on schedule for August
SSHS	Network servers moved to First Floor-had initial meeting, should be completed on time
SSHS	Elevator replacement-elevator ordered will determine time to install
SSHS	Woodshop paint room exhaust fan-scheduled for last week of July
SSHS	Paint Science research room-will be done by early August
SSHS	Cabinetry for research room-we have the cabinets will install after consulting teacher and paint is completed



HS main entrance



SSMS-Capital Upgrades

SSMS	Handicapped Access at Main Entrance-in progress old concrete being removed
SSMS	Replace asphalt in parking lot-in progress
SSMS	Replace/repair auditorium ceiling-more damage than expected working on a solution, I have meeting with JS and the contractor next week
SSMS	Remove floor tile in room 116 and replace with new tile-material delivered...waiting on date for install
SSMS	Repair walls and paint Principal's office-completed
SSMS	Pave area under bleachers-in progress
SSMS	Social Worker Office set up-floor and supplies delivered last week...install sometime early August
SSMS	Repair A/C in room 155-In house-early August
SSMS	Replace floor in room 118-on order-delivered last week
SSMS	New Drop Ceiling in rooms 118 & 120-in process-just need lights installed











Capital Work Updates-COVERT

Covert	New LED lighting in hallways and in Rooms 111, 112, 113, 114, 115-Material ordered..waiting on the start date
Covert	Floor replacement 4 classrooms (109/110/111/112)-scheduled upon completion at Hewitt
Covert	Auditorium projector and speakers- delayed shipment, expected install in August



Hewitt Capital Projects

Hewitt	Primary Playground-scheduled early August
Hewitt	Floor replacement Rooms 4, 29 and 8-completed
Hewitt	Faculty room floor and replace with new tile-scheduled for 7-22
Hewitt	Ceiling installation rooms 21, 26, 27, 28 and 29-in progress
Hewitt	Drop ceiling installation in the hallways-scheduled for after the summer program-mid August







Riverside Capital Projects

Riverside	Faculty room renovation-demo is done, refurbish starts Monday
Riverside	Painting of blacktop to create play area-scheduled Mid August
Riverside	3 classroom bathrooms to be updated-tiling in progress
Riverside	Principal's bathroom needs to be updated-Epoxy flooring is completed
Riverside	5 bathrooms epoxy flooring-completed
Riverside	Powerwash exterior spots-completed
Riverside	Paint Pillars in front of building-completed
Riverside	Air compressor for the univent systems-scheduled mid-August



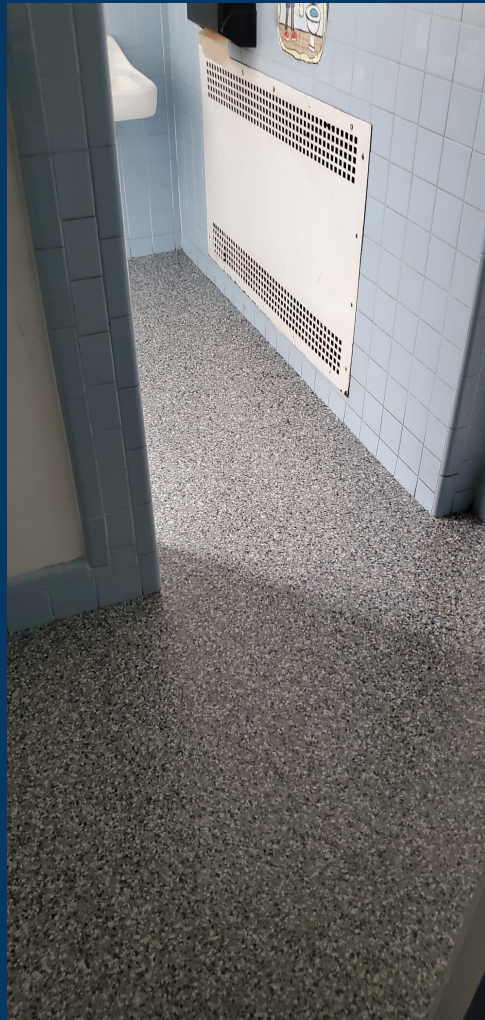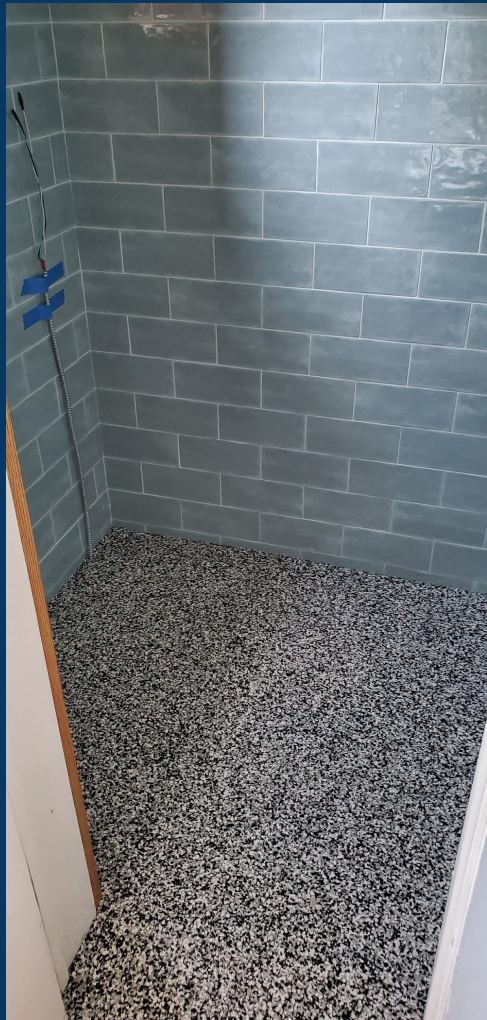

Capital Upgrades-Watson

Watson	Improve exterior lighting in the courtyard-lights purchased, awaiting install in Mid-August
Watson	Repair/repave walkway in the alley-scheduled Mid August
Watson	Replace stage curtains-awaiting delivery
Watson	Repair/replace walkway in front of the building-scheduled Mid August
Watson	Project Great Camera-scheduled for this week



Wilson Capital Upgrades

Wilson	Playground Replacement-scheduled early August
Wilson	Playground blacktop area repair or replace with turf-scheduled early August
Wilson	Auditorium projector and speakers-expected in August
Wilson	Boys/Girls Bathroom Floor Replacements (10)-in progress-7 completed...last three scheduled this week



